


BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Providing CC Road and Drains at Behind ACP office Basavalingappanagara in ward No. 05 Byatarayanapura Sub Division	
2	Estimate Cost	30.00 Lakhs ✓	
3	Administrative Approved No and Date	594/13-14, Date. 23.12.2013 ✓	
4	Technical sanction No. and Date	86/13-14, Date. 23.12.2013 ✓	
5	Job Code No. and P Code No.	005-14-000061 ✓	
6	Tender Direct Entrested to KRIDL	KRIDL ✓	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable ✓	
8	Tender Approved Details	Not Applicable ✓	
9	Work Order No and Date	509/2013-14, Date. 24.02.2014 ✓	
10	Stipulation time of Completion	60 Days ✓	
11	Actiual Date of Commencement	01.07.2014	
12	Actiual Date of Completion	30.08.2014	
13	Delay if any	Nil ✓	

	on for Delay	Nil	
	Payment made till date.	Nil	
16	Status of Work	Completed ✓	
17	Photograph verified	Enclosed ✓	
18	Date of Inspection	04.08.2015 ✓	
19	MB No. and Page No.	Mb No. 2501 Page No. 250036-250045 ✓	
20	BR No and Date	313/30.08.2014 ✓	
21	Test Result	Quality Test Report submitted by Civil Tech Consultants and Engineers is verified and Enclosed ✓	
22	Section officer	Sri P A Chandrakanthraju AE	
23	Sub Division Officer	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactroy	
b	Comments	Work completed as per MB	


 Y C Kale gowda
 Executive Engineer (Retd)




qy
AE-05

← 2c F



qy
AE-05

← 2c F

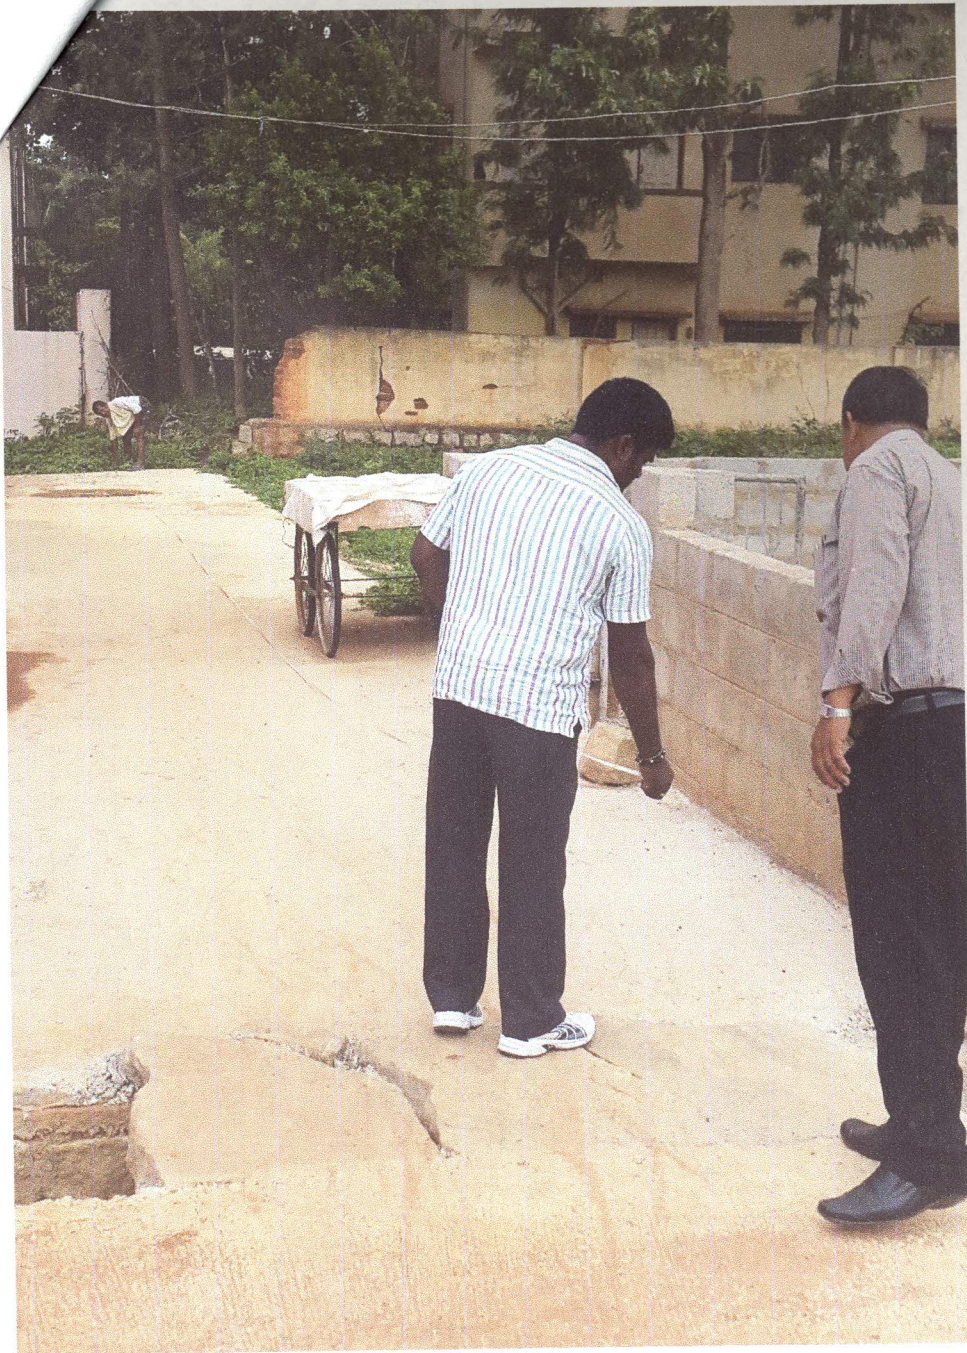

94
TAE-05

7 22
